

OFFICIAL RECORD

Requested By:
DC/COMMUNITY DEVELOPMENT

Assessor's Parcel Number: N/A

Date: AUGUST 26, 2011

Recording Requested By:

Douglas County - NV
Karen Ellison - Recorder
Page: 1 Of 6 Fee: 0.00
BK-0811 PG- 5287 RPTT: 0.00



Name: JEANE COX, COMMUNITY DEVELOPMENT

Address: _____

City/State/Zip: _____

Real Property Transfer Tax: \$ N/A

CHANGE ORDER NO 4 (#2011.216)

(Title of Document)

CHANGE ORDER

No. 4

FILED
2011. 216

2011 AUG 26 PM 2:42

PROJECT: Lake Village Ph II Water Quality Improvement Project- EIP Project #679
PWP-DO-2010-262

DATE OF ISSUANCE: July 5, 2011 EFFECTIVE DATE: July 5, 2011

FEDERAN
2011
[Signature]

OWNER: Douglas County Utilities

OWNER's Contract No. PWP-DO-2010-262

CONTRACTOR: Peek Construction ENGINEER: Nichols Consulting Engineers, Chtd.

You are directed to make the following changes in the Contract Documents:

Description: 1. remove & replace the 18" CMP at sta+/-13+75 with 18" RCP; do not video the existing pipe.

Reason for Change Order: Work to adjust to field conditions and adjust time for delays to date.

Attachments: Copy of portions of sheet #C8, tabulation of line items involved in the work.

CHANGE IN CONTRACT PRICE:	CHANGE IN CONTRACT TIMES:
Original Contract Price <u>\$1,241,781.50</u>	Original Contract Times Substantial Completion: <u>September 16, 2011</u> Ready for final payment: <u>September 30, 2011</u>
Net changes from previous Change Orders No. 1 to No. 3 <u>\$32,269.07</u>	Net change from previous Change Orders No. N/A to No. N/A <u>3 days</u>
Contract Price prior to this Change Order <u>\$1,274,050.57</u>	Contract Times prior to this Change Order Substantial Completion: <u>September 19, 2011</u> Ready for final payment: <u>October 3, 2011</u>
Net Increase of this Change Order <u>\$6,441.00</u>	Net Increase of this Change Order <u>14 days</u>
Contract Price with all approved Change Orders <u>\$1,280,491.57</u>	Contract Times with all approved Change Orders Substantial Completion: <u>October 4, 2011</u> Ready for final payment: <u>October 18, 2011</u>

RECOMMENDED:
By: *[Signature]*
Engineer (Authorized Signature)

APPROVED:
By: *[Signature]*
Owner (Authorized Signature)

ACCEPTED:
By: *[Signature]*
Contractor (Authorized Signature)

Date: July 5 2011


Date: 23 Aug. 2011

Date: 8/1/2011

Add 18" rcp

description	\$/unit	# units	add	deduct
18" rcp line item #37	\$ 81.00	65	\$ 5,265.00	
flared end section #35	\$ 630.00	2	\$ 1,260.00	
AC saw cut #7	\$ 1.50	160	\$ 240.00	
AC remove #8 \$/tn	\$ 27.00	7	\$ 189.00	
AC pavement #13 \$/tn	\$ 140.00	3.3	\$ 462.00	
remove exist cmp #46	\$ 70.00	65	\$ 4,550.00	
vidio ex SD #49	\$5,525.00	1		\$ 5,525.00
			\$11,966.00	\$ 5,525.00
		total	\$ 6,441.00	



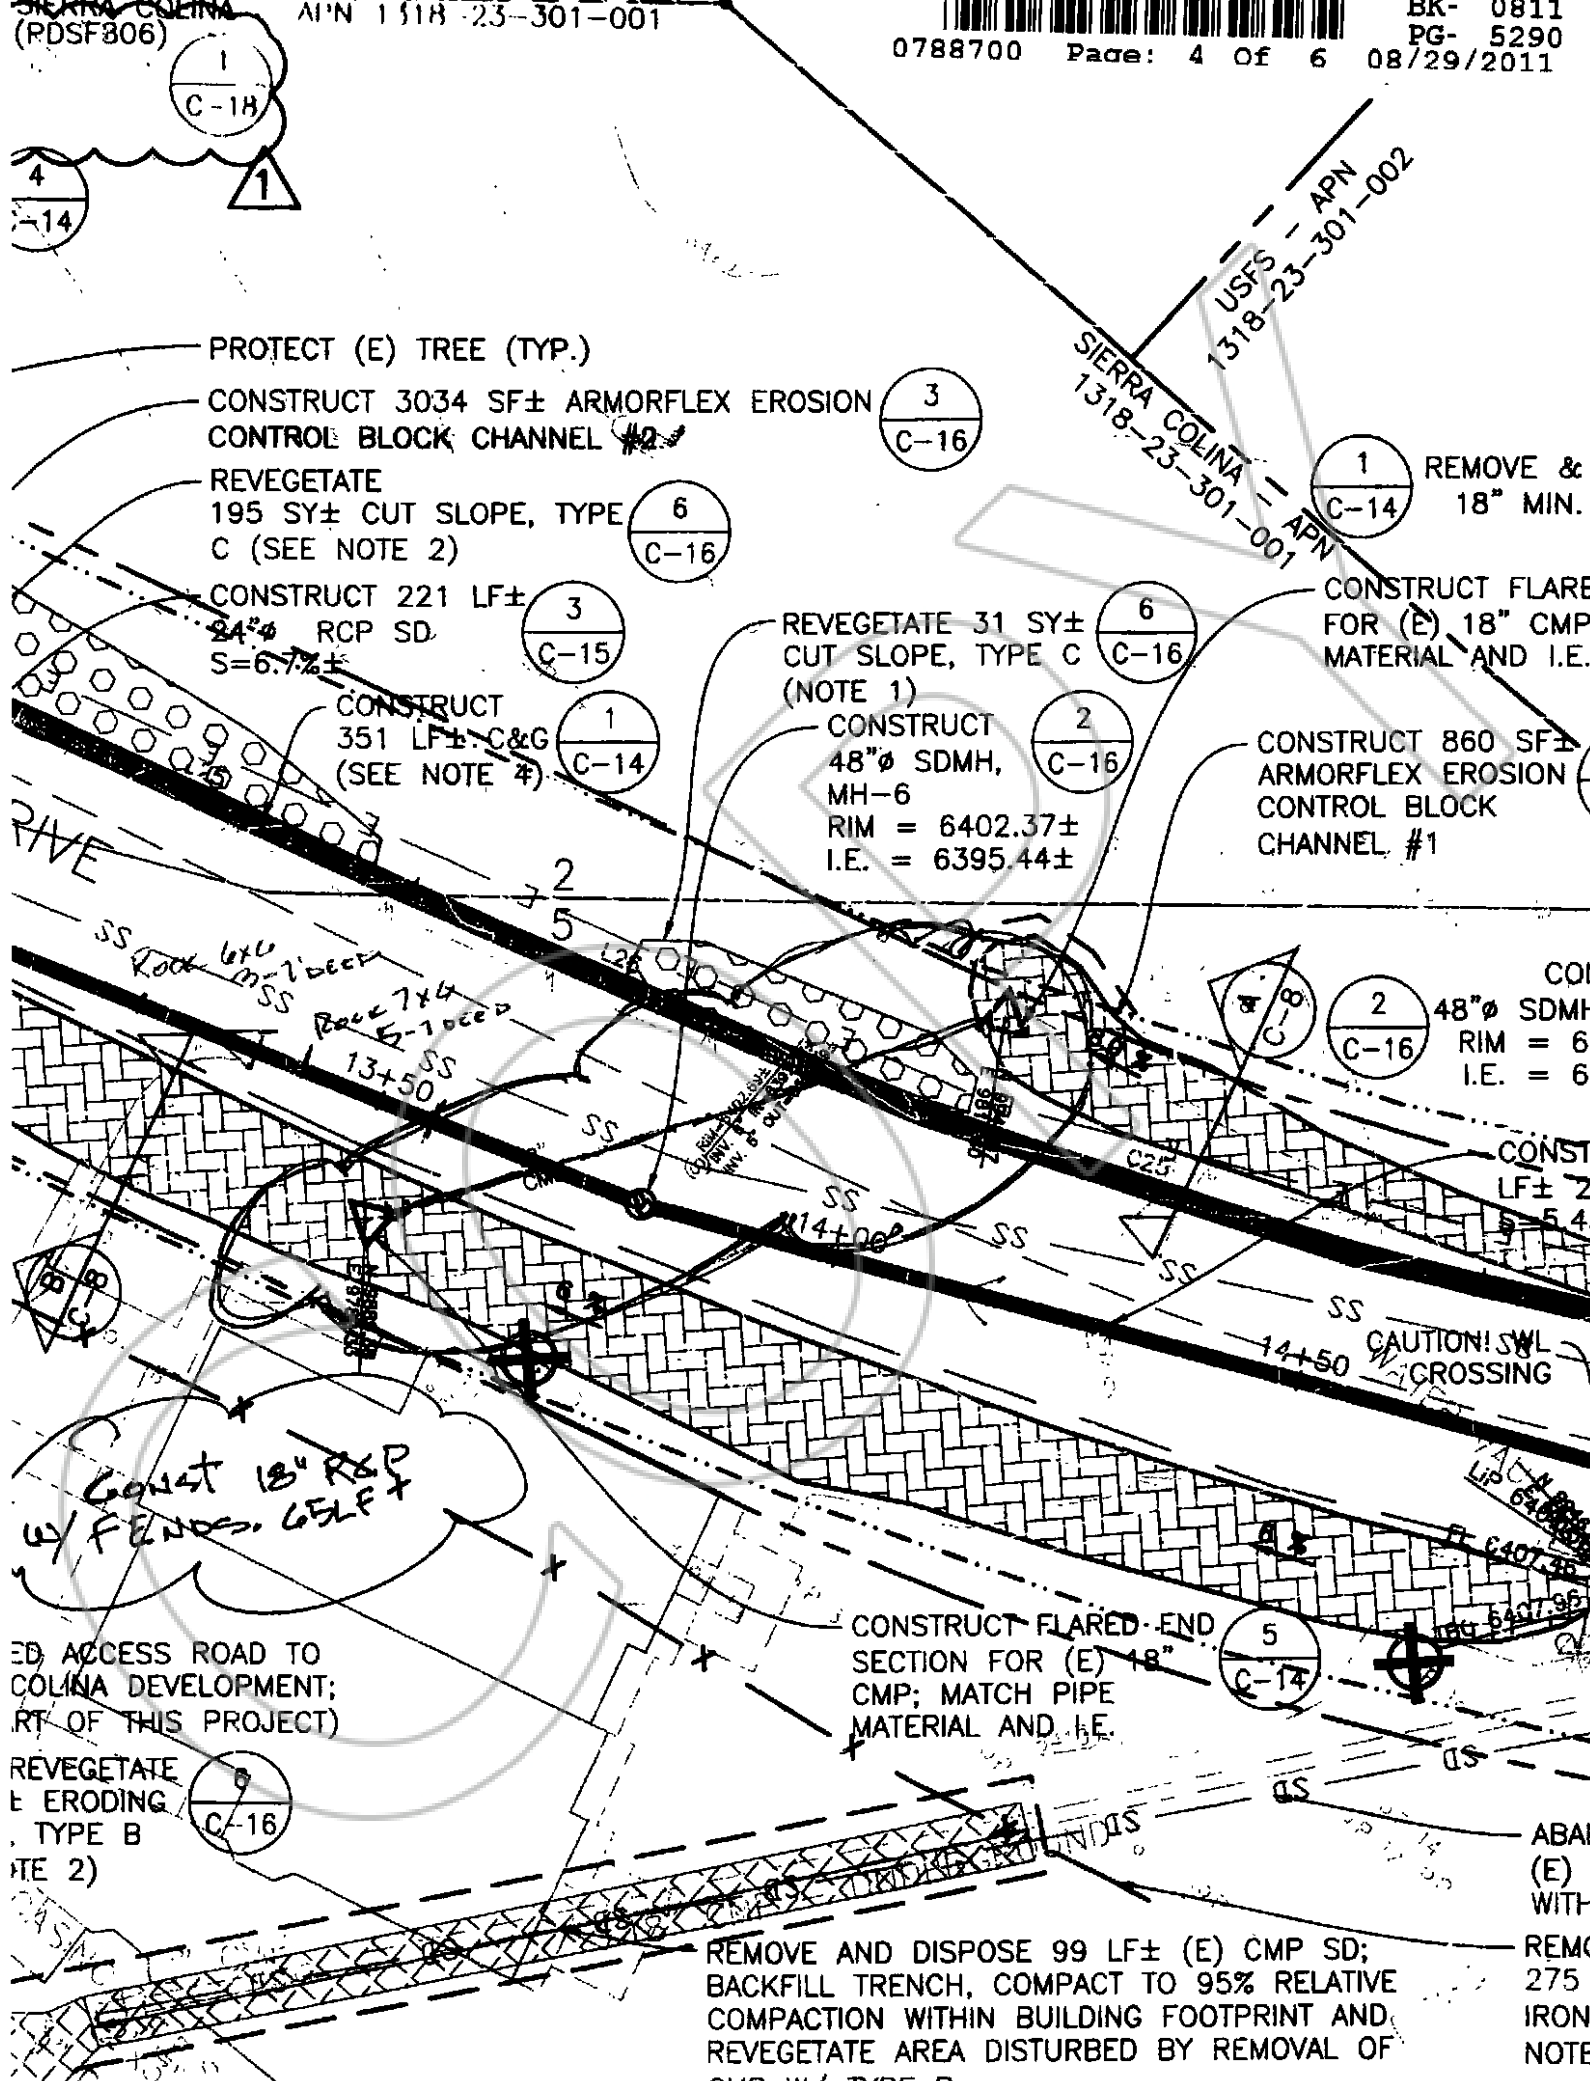

PROTECT (E) TREE (TYP.)

CONSTRUCT 3034 SF± ARMORFLEX EROSION CONTROL BLOCK CHANNEL #2

REVEGETATE 195 SY± CUT SLOPE, TYPE C (SEE NOTE 2)

CONSTRUCT 221 LF± 24" RCP SD. S=6.7%±

CONSTRUCT 351 LF± C&G (SEE NOTE 4)

REVEGETATE 31 SY± CUT SLOPE, TYPE C (NOTE 1)

CONSTRUCT 48"Ø SDMH, MH-6 RIM = 6402.37± I.E. = 6395.44±

CONSTRUCT 860 SF± ARMORFLEX EROSION CONTROL BLOCK CHANNEL #1

CONSTRUCT 48"Ø SDMH RIM = 6 I.E. = 6

CONSTRUCT LF± 2

CAUTION! SWL CROSSING

CONSTRUCT FLARED-END SECTION FOR (E) 18" CMP; MATCH PIPE MATERIAL AND I.E.

ED ACCESS ROAD TO COLINA DEVELOPMENT; RT OF THIS PROJECT)

REVEGETATE ERODING TYPE B (NOTE 2)

REMOVE AND DISPOSE 99 LF± (E) CMP SD; BACKFILL TRENCH, COMPACT TO 95% RELATIVE COMPACTION WITHIN BUILDING FOOTPRINT AND REVEGETATE AREA DISTURBED BY REMOVAL OF

ABAN (E) WITH REMC 275 IRON NOTE

PROPOSED ACCESS ROAD TO SIERRA COLINA DEVELOPMENT;
(NOT PART OF THIS PROJECT)

FILL & REVEGETATE
297 SY± ERODING
DITCHES, TYPE B
(SEE NOTE 2)

2
C-16

REMOVE AND
BACKFILL TR
COMPACTION
REVEGETATE
CMP W/ TY

1378.9
25
1353.9

13+50

Do Not VIDEO; R & R w/ 18" RCP

2
C-16

CONSTRUCT MH-6
I.E. = 6395.44±

CAUTION! 18" CMP STORM DRAIN
CROSSING; PROTECT IN PLACE; VIDEO
SURVEY PIPE AND SUBMIT VIDEO TO
OWNER; REMOVE AND REPLACE IF
NECESSARY (ALTERNATE BID ITEM)

MH-6
STA 13+78.95
RIM 6402.37
INVERT IN 6395.44 PIPE
INVERT OUT 6395.44 PIPE

EGL @ 10-YEAR EVENT
HGL @ 10-YEAR EVENT

SLOPE 6.70%

DIA 24in.RCP

CONSTRUCT 24"Ø
RCP SD



EK- 0811
PG- 5291

12+50

13+00

13+50



COPY

CERTIFIED COPY

The document to which this certificate is attached is a full, true and correct copy of the original on file and on record in my office.

DATE: Aug 26 2011
Clerk of the Judicial District Court
of the State of Nevada, in and for the County of Douglas.
By [Signature] Deputy
