

Doc Number: 0809218

09/17/2012 01:08 PM

OFFICIAL RECORDS

Requested By

De/PUBLIC Works

DOUGLAS COUNTY RECORDERS

Karen Ellison - Recorder

Page 1 Of 6 Fee: 0.00

Bk 0912 Pg 3740



0809218

Deputy: ke

Assessor's Parcel Number: N/A

Date: SEPTEMBER 17, 2012

Recording Requested By:

Name: JEANE COX, PUBLIC WORKS

Address: _____

City/State/Zip: _____

Real Property Transfer Tax: \$ N/A

CHANGE ORDER NO 2 (#2012.207)

(Title of Document)

This page added to provide additional information required by NRS 111.312 Sections 1-2. (Additional recording fee applies)

This cover page must be typed or legibly hand printed.

CHANGE ORDER

No. 2

PROJECT: Lake Village Ph II-A Water Quality Improvement Project

DATE OF ISSUANCE: August 30, 2012 EFFECTIVE DATE: August 30, 2012

OWNER: Douglas County Nv

OWNER's Contract No. PWP-DO-2012-232

CONTRACTOR: Spieß Construction Co. Inc. ENGINEER: RO Anderson

2012 SEP 17 AM 9:55
 FILED
 10-20-2012
 TERRY RAN
 CLERK
 DEPUTY

You are directed to make the following changes in the Contract Documents.

Description: Add Rip-Rap ditch to lower end of Armor-flex Channel per attached drawing, \$8,156.50.

Reason for Change Order: Neither the plans nor specifications address protecting the +/-32ft. from end of Armor-flex to the NDOT R/W; this portion of channel needs to be protected to provide a complete project.

a. to

Attachments: Contractor's COR #21218-001.

<p>CHANGE IN CONTRACT PRICE:</p> <p>Original Contract Price</p> <p><u>\$270,007.20</u></p>	<p>CHANGE IN CONTRACT TIMES:</p> <p>Original Contract Times</p> <p>Substantial Completion: <u>October 15, 2012</u></p> <p>Ready for final payment: <u>October 30, 2012</u></p>
<p>Net changes from previous Change Orders No. 1</p> <p><u>\$400.00</u></p>	<p>Net change from previous Change Orders No. 1</p> <p style="text-align: center;"><u>0</u> days</p>
<p>Contract Price prior to this Change Order</p> <p><u>\$270,407.20</u></p>	<p>Contract Times prior to this Change Order</p> <p>Substantial Completion: <u>October 15, 2012</u></p> <p>Ready for final payment: <u>October 30, 2012</u></p>
<p>Net Increase of this Change Order</p> <p><u>\$8,156.50</u></p>	<p>Net Increase of this Change Order</p> <p style="text-align: center;"><u>0</u> days</p>
<p>Contract Price with all approved Change Orders</p> <p><u>\$278,563.70</u></p>	<p>Contract Times with all approved Change Orders</p> <p>Substantial Completion: <u>October 15, 2012</u></p> <p>Ready for final payment: <u>October 30, 2012</u></p>

RECOMMENDED:
By: [Signature]
Engineer (Authorized Signature)

APPROVED:
By: [Signature]
Owner (Authorized Signature)

ACCEPTED:
By: [Signature]
Contractor (Authorized Signature)

Date: Aug 30 2012
Page 1

Date: 9-11-12

Date: 9/6/2012



AZ #119975 • CA #333989 • NV #0038929

Spiess Construction Co., Inc.

P.O. Box 2849
Santa Maria, CA 93457-2849
(805) 937-5859
Fax (805) 934-4432

DOUGLAS COUNTY COMMUNITY DEVELOPMENT
1594 ESMERALDA AVE., ROOM 202
MINDEN, NV 89423

LAKE VILLAGE PHASE II-A WATER QUALITY
IMPROVEMENT PROJECT
EIP PROJECT #679

CHANGE ORDER REQUEST NO. 21219-001

SCOPE: Furnish and install additional rip rap as directed by the Owner to the lower drainage area section from end of Armorflex Block to NDOT right-of-way. Proposed work includes: Clear & Grubb Material Removal, Geo Fabric Installation, 1 1/2" - 2" rip-rap rock. Rip rap rock placement shall be approximately 12" thick.

<u>ADD:</u>			
Additional Rip Rap	1	LS	<u>\$7,415.00</u>
Subtotal			\$7,415.00
General Contractor Markup 10%			741.50
TOTAL CHANGE ORDER REQUEST 21219-001			\$8,156.50

TIME EXTENSION REQUESTED: 6 Work Days

SPIESS CONSTRUCTION CO., INC.

SUBMITTED BY: Scott A. Coleman DATE: 23 August 2012
Scott A. Coleman, Project Manager



KEVIN O'BRIEN CONSTRUCTION LLC

General Engineering Contractor

P.O. Box 3043
Gardnerville, Nevada 89410
(775) 309-9498

Nevada License #0071829

California License #348243

PROPOSAL

Customer:	Spieess Construction Co, Inc P.O. Box 2849 Santa Maria, CA 93457	Job:	Lake Village Phase II-A Water Quality Improvement Project
Attn:	Scott Coleman	Re:	Change Order #2
Date:	August 22, 2012		

SCOPE OF WORK:



Rip rap lower drainage area section from end of Amorflex block to NDOT right-of-way.

Proposed work includes:

- Clear & grub / material removal
- Geo fabric installation
- 1 1/2"-2" rip-rap rock
- 12" (approximately) rip-rap rock placement

PROPOSAL TOTAL

\$ 7,415.00

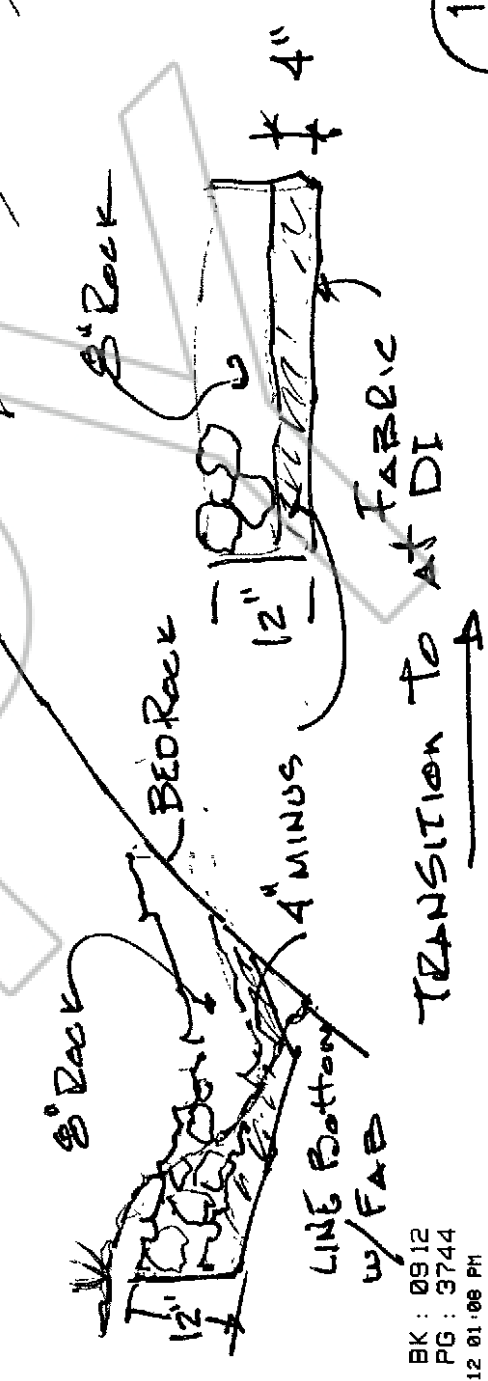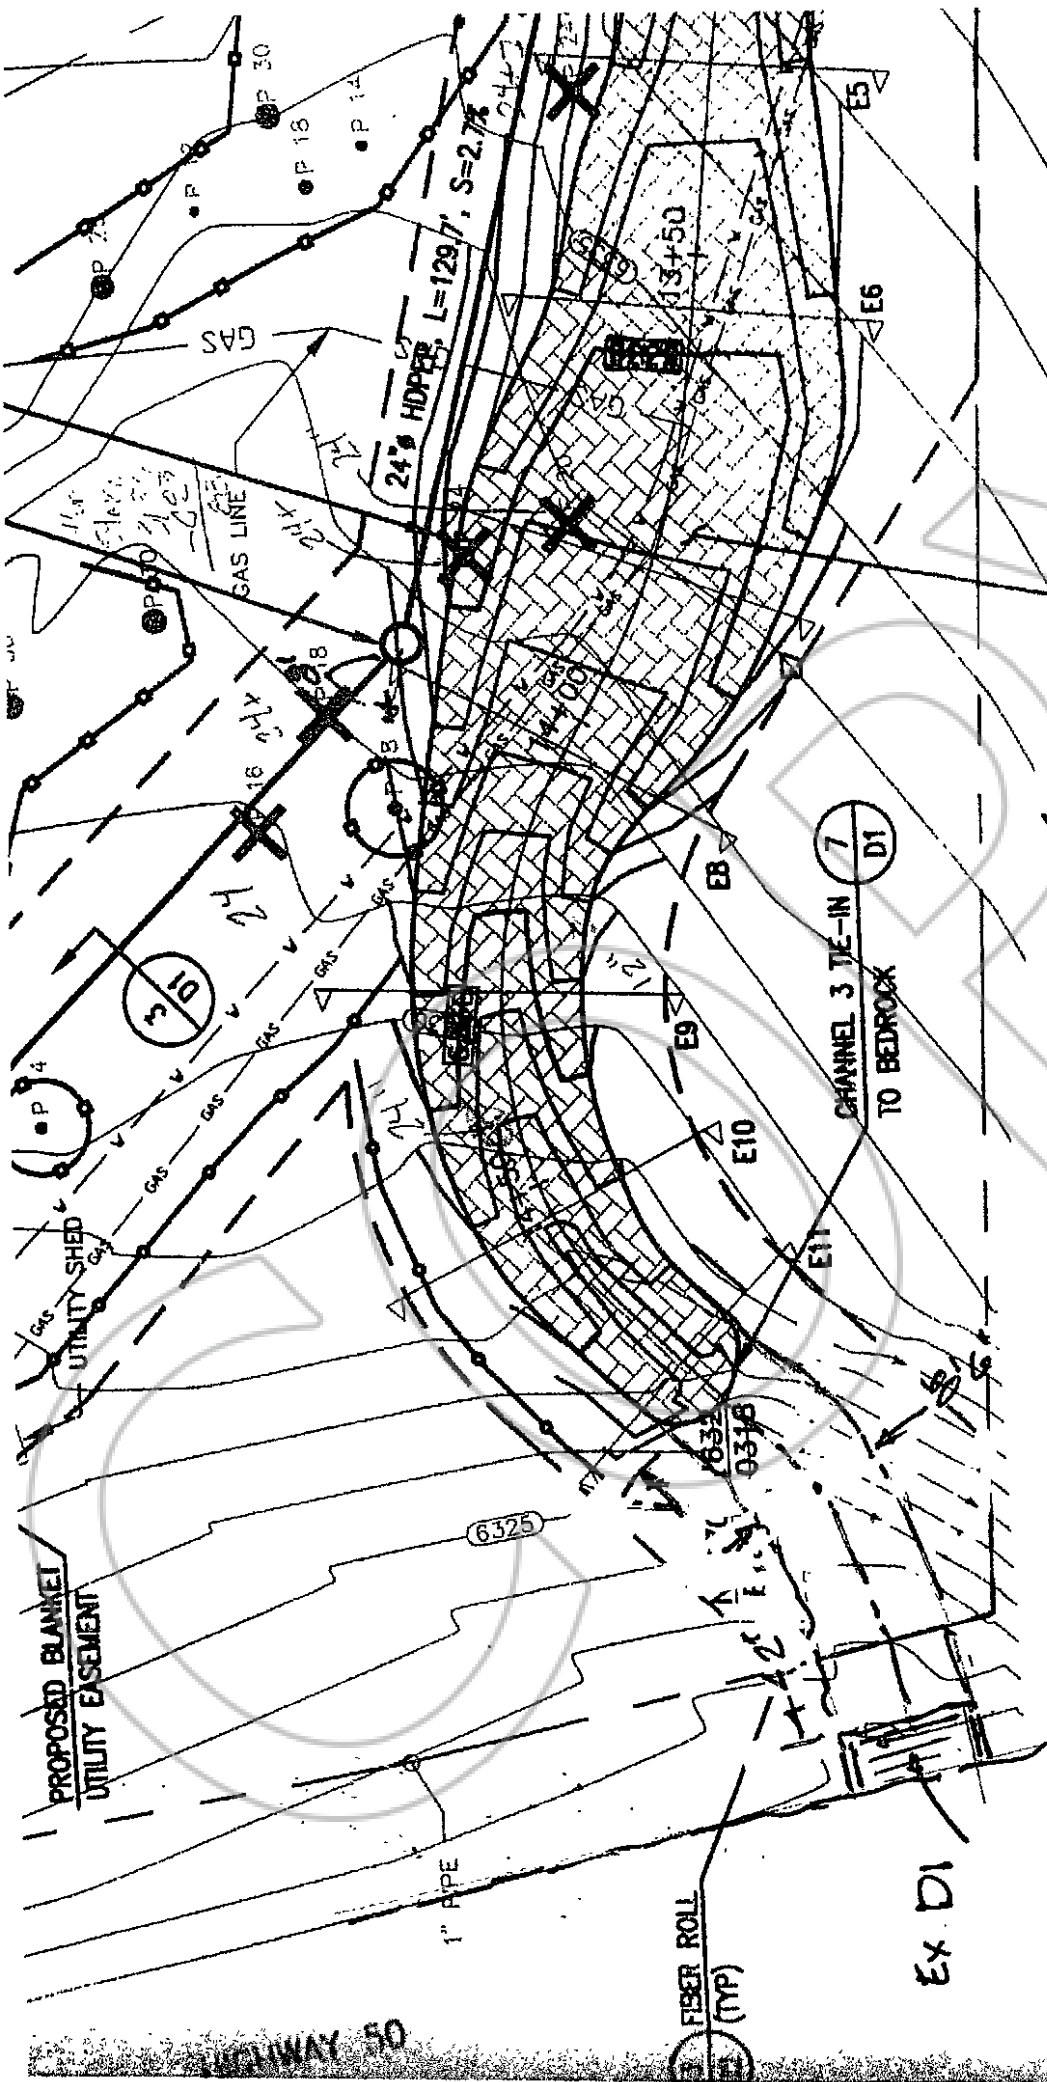

PROPOSED BLANKET
UTILITY EASEMENT

D1 3

CHANNEL 3 TE-IN 7
TO BEDROCK
D1 7

FIBER ROLL
(MP)

Ex D1

US 50

BK : 0912
PG : 3744

09/17/2012 01:06 PM





COPY

CERTIFIED COPY

The document to which this certificate is attached is a full, true and correct copy of the original on file and on record in my office.

DATE: Sept 17, 2012

THAN Clerk of the 9th Judicial District Court
of the State of Nevada, in and for the County of Douglas.

By David J. Muloch Deputy
